


Highways Division

South Maui Community Plan Advisory Committee Meeting

November 9, 2022




Highways Division

Existing Construction Projects


- **Piilani Highway/Kulanihako'i Street Roundabout**
 - Northbound lanes completed September 19, 2022
 - Southbound lanes anticipated to be completed mid-December 2022; roundabout will be fully operational
 - All remaining work (shoulder/median) anticipated to be completed January/February 2023
 - <https://hidot.hawaii.gov/highways/roundabouts/>






Highways Division Upcoming Projects


Roundabout Traffic Flow - Northbound

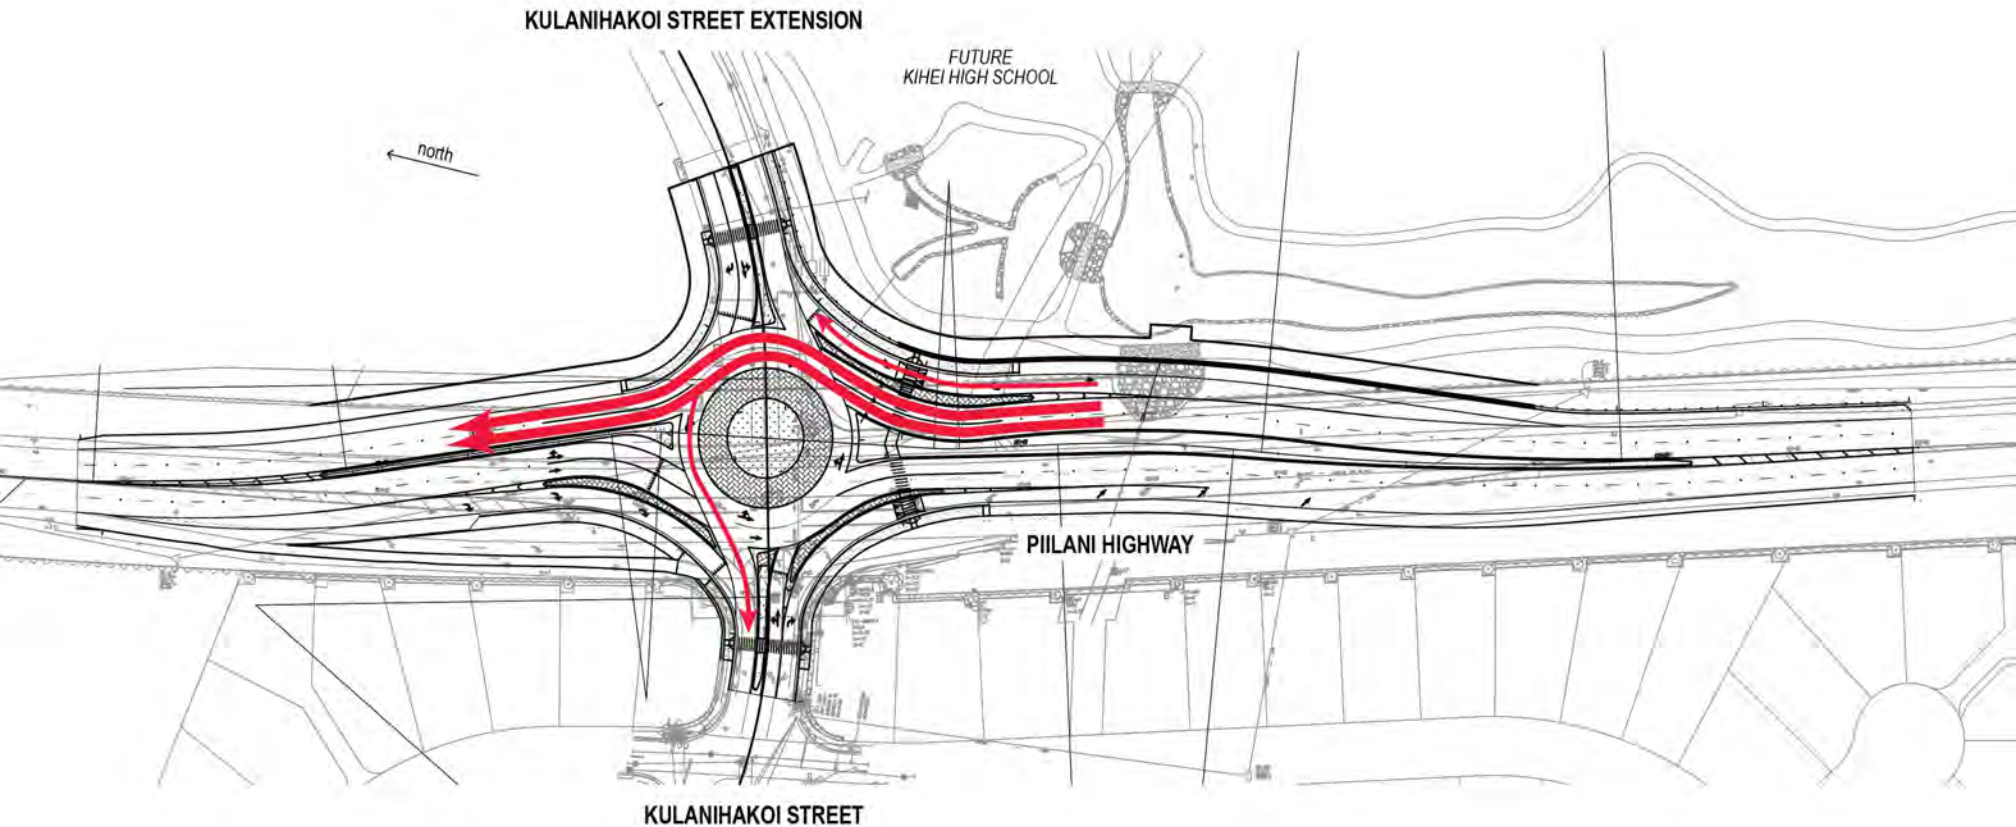



Highways Division Upcoming Projects


Roundabout Traffic Flow - Southbound

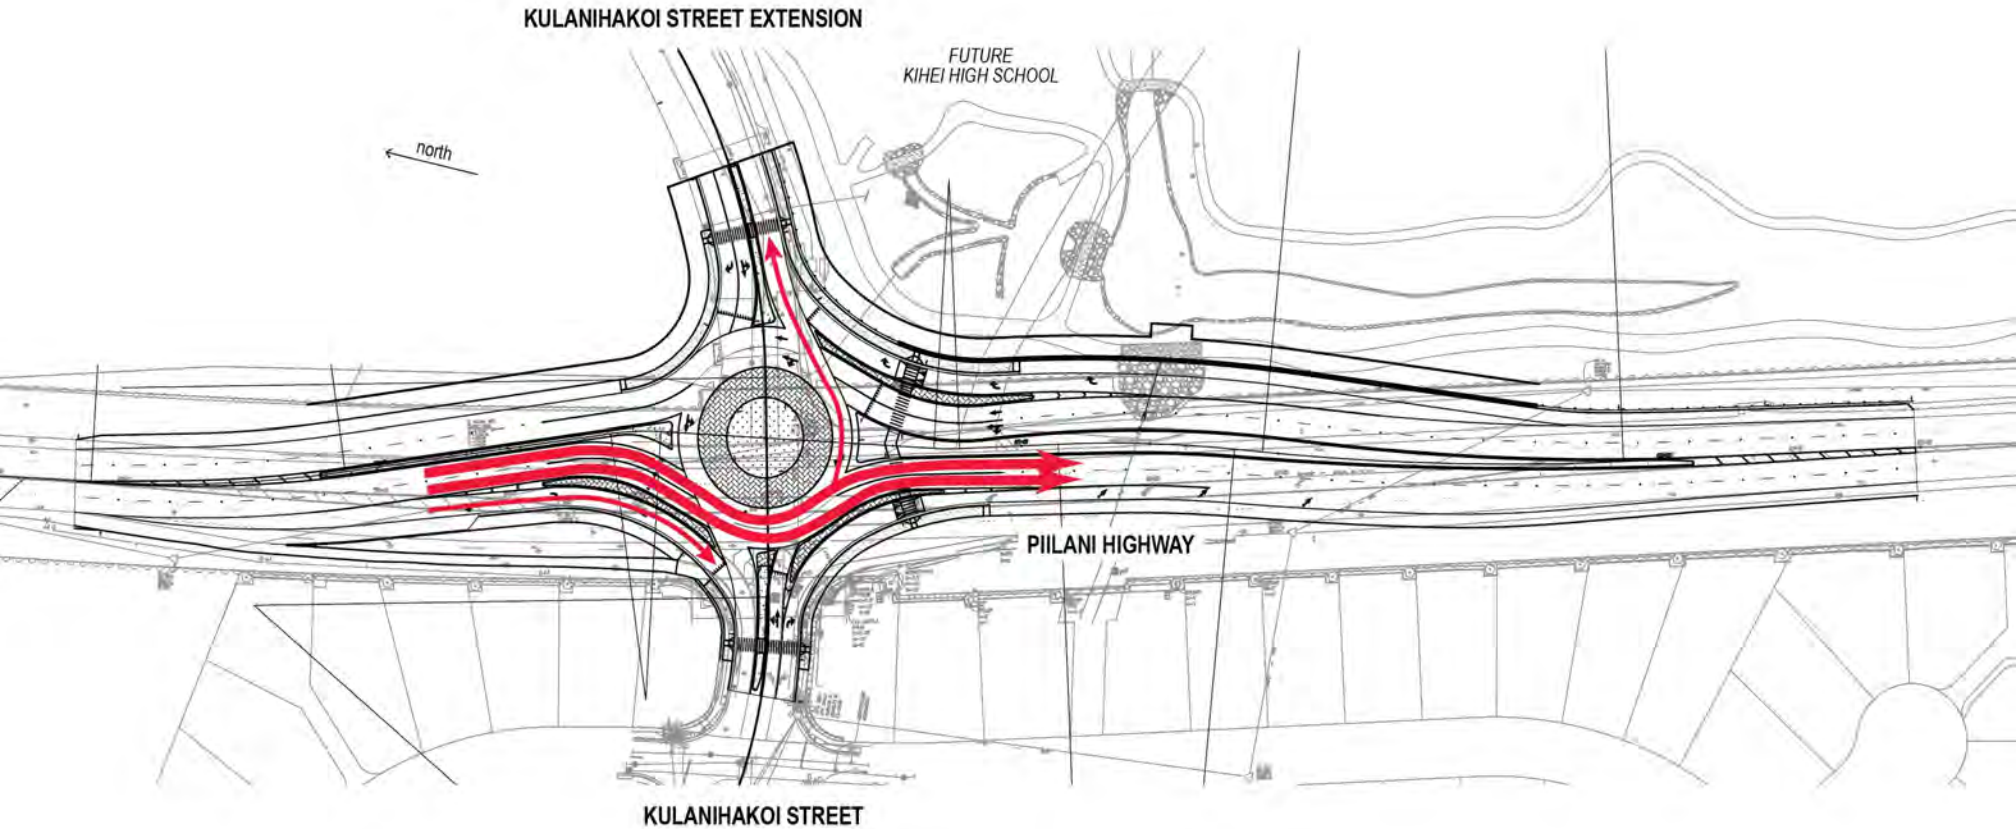




Highways Division Upcoming Projects


Roundabout Traffic Flow - Eastbound

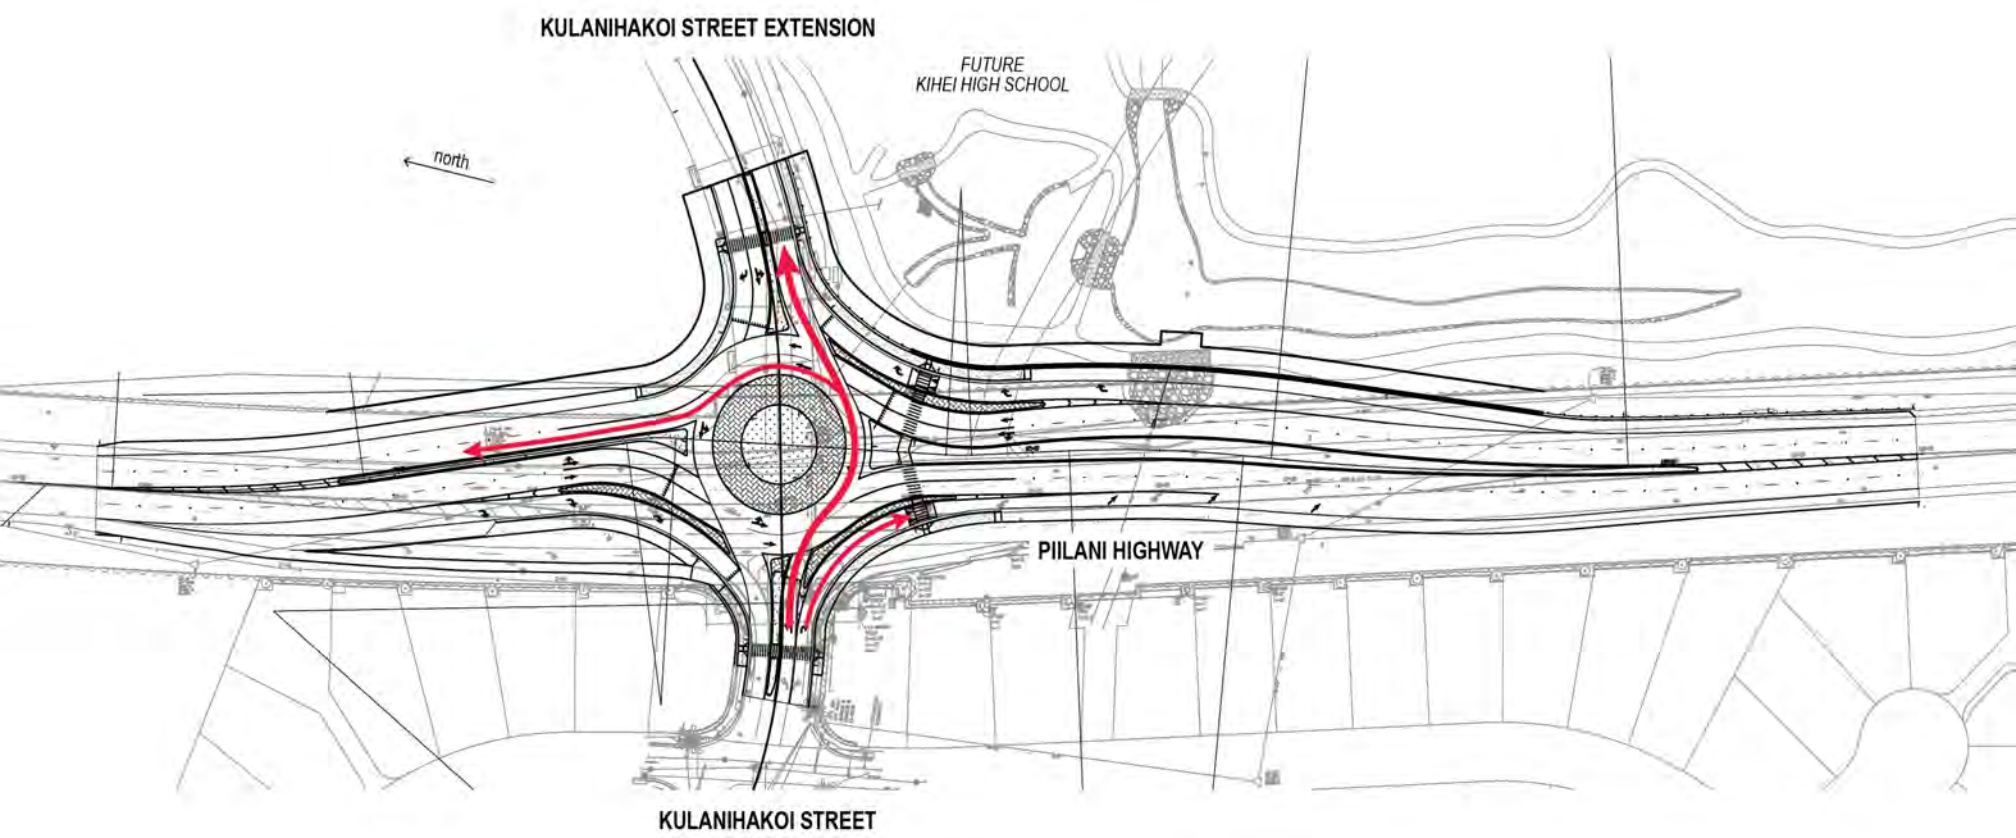




Highways Division Upcoming Projects


Roundabout Traffic Flow - Westbound

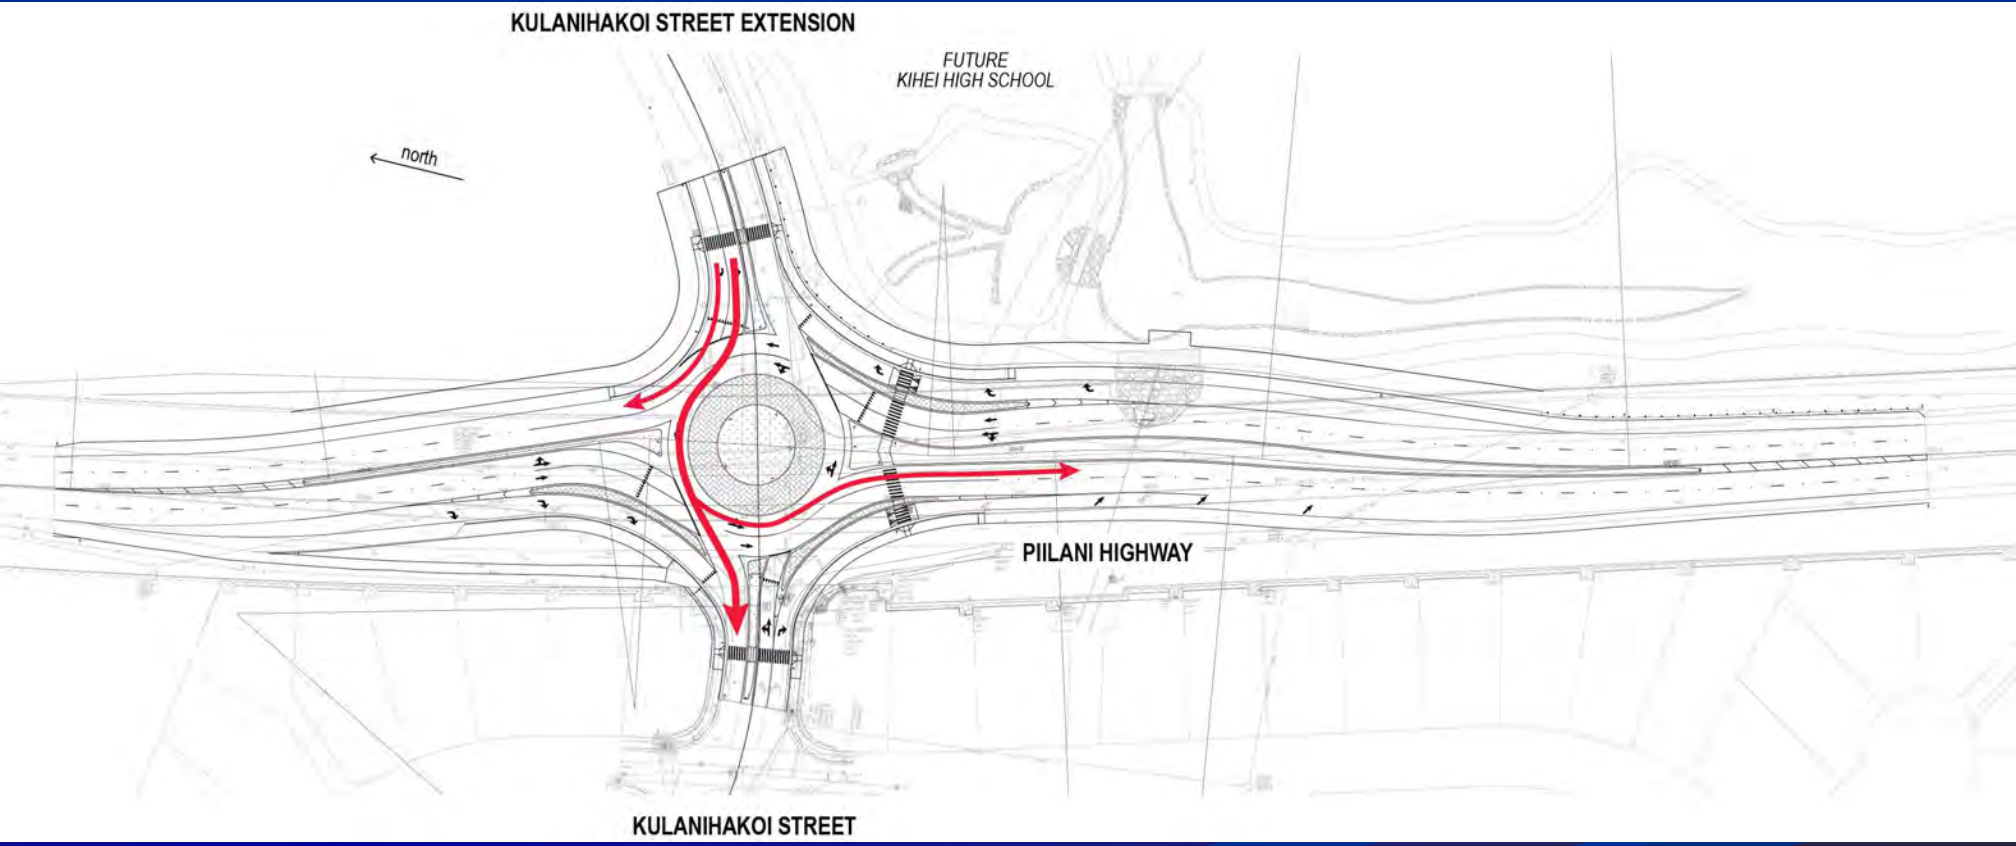




Highways Division Upcoming Projects


Roundabout - Bicycle User Accommodations

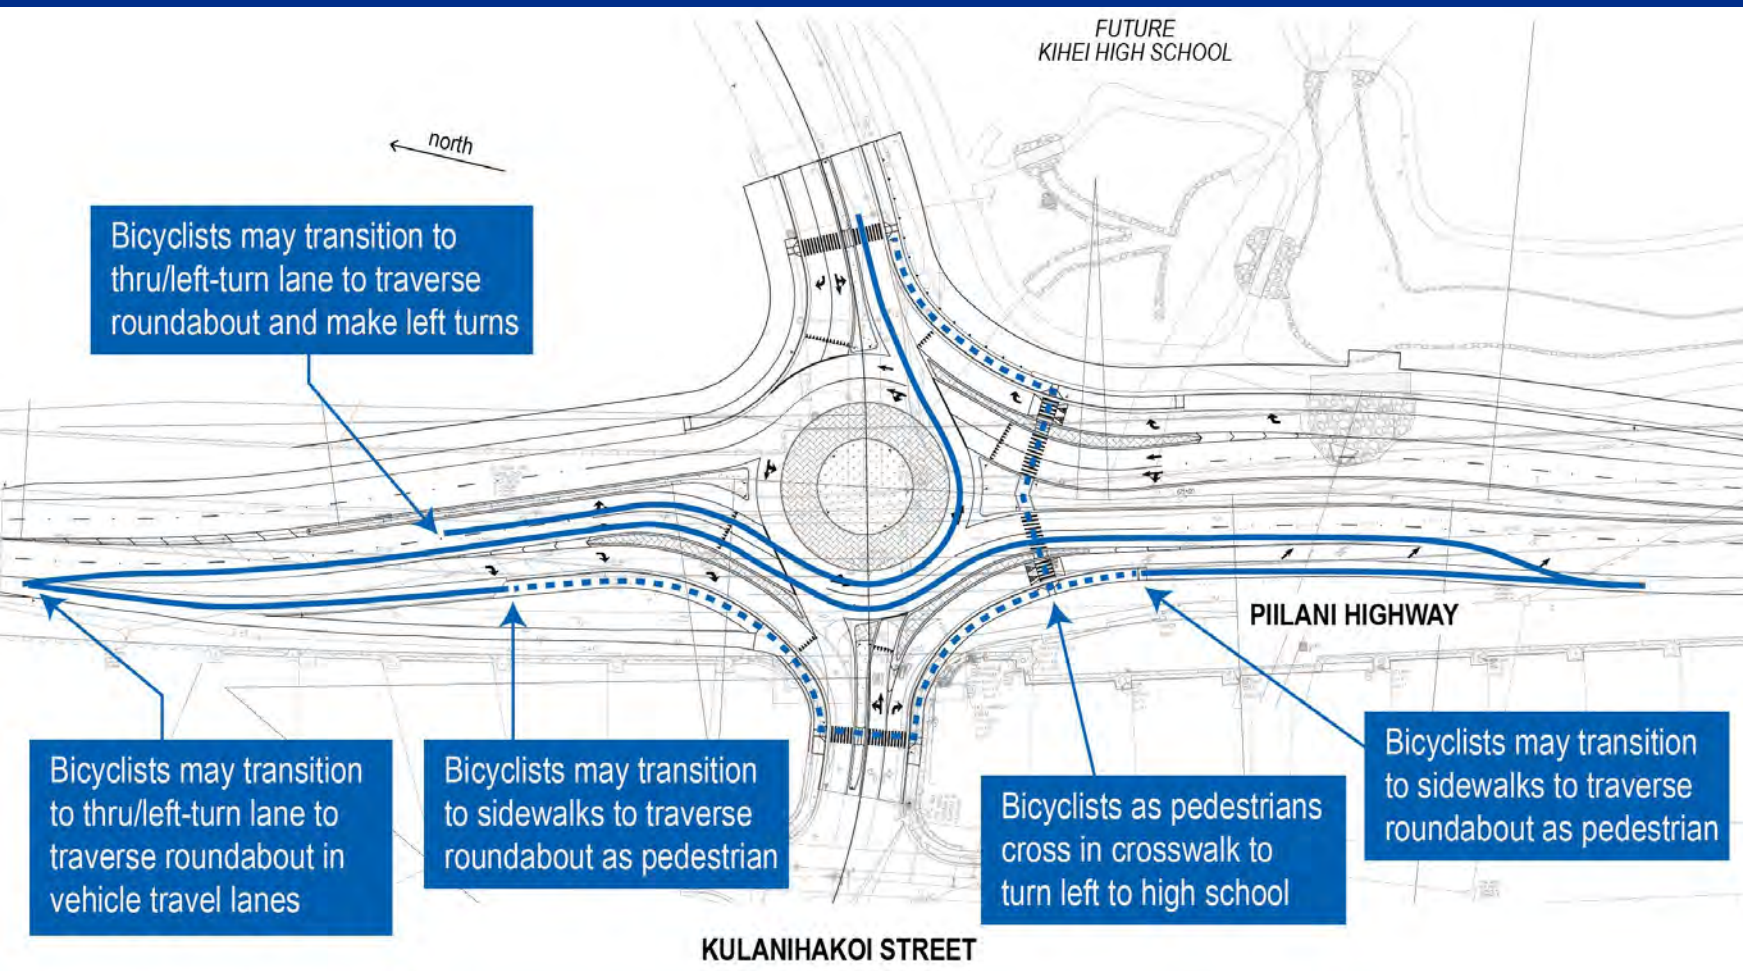




Highways Division Upcoming Projects


Roundabout - Pedestrian User Accommodations

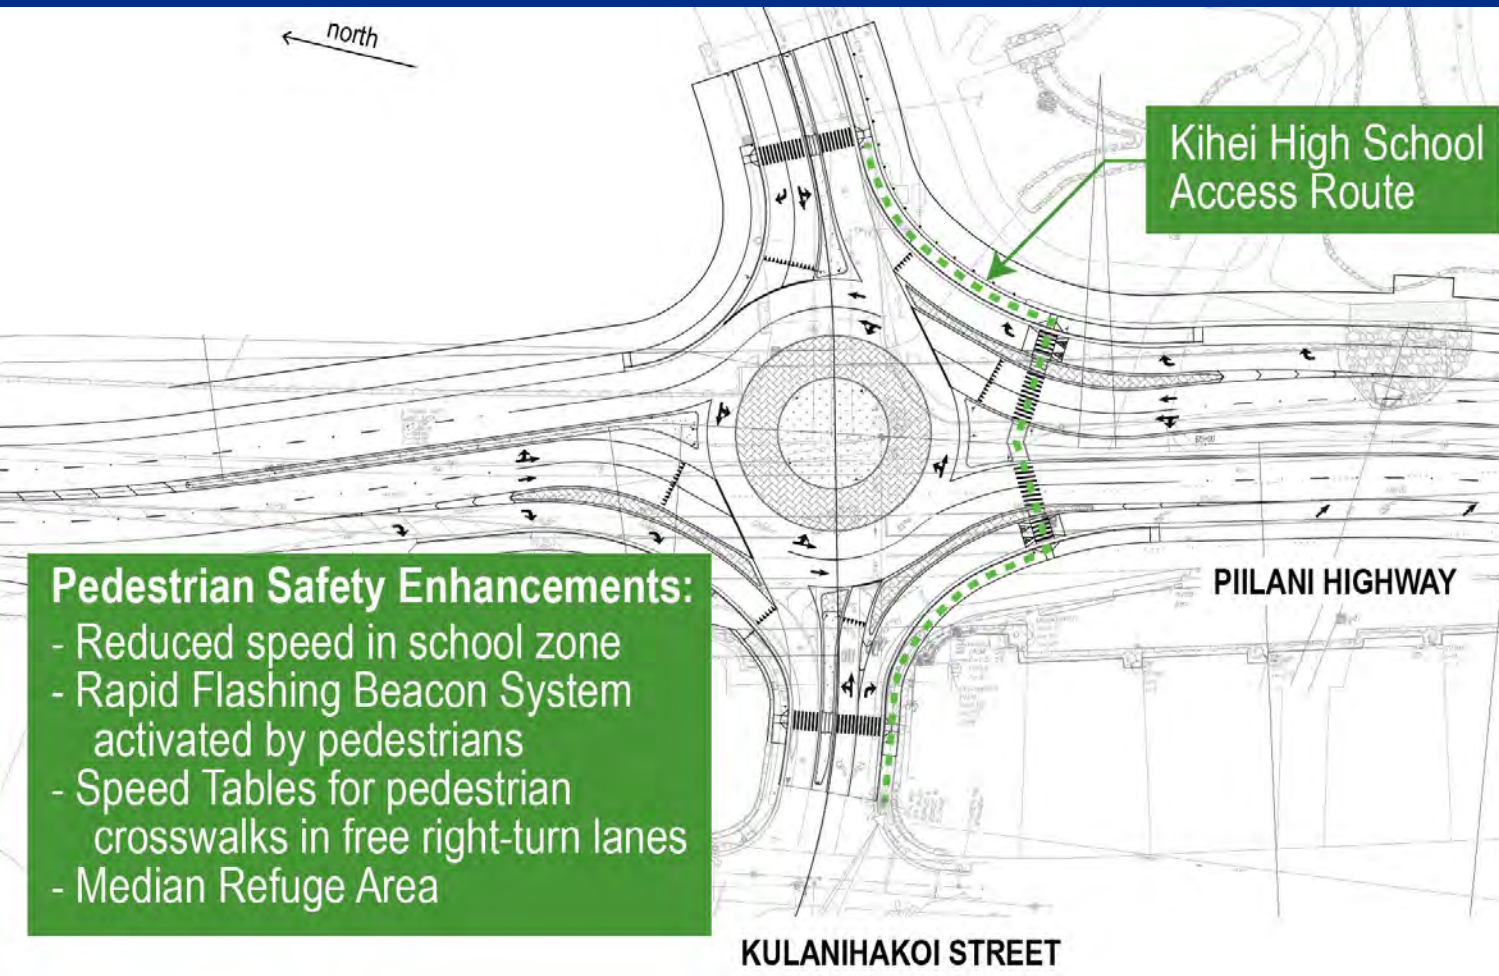




Highways Division
Upcoming Projects

- **Piilani Highway/Okolani Drive/Mikioi Place Traffic Signal**
 - **Estimated construction – January/February 2023**
- **Piilani Highway/Moi Place Intersection Lighting**
 - **Design at 60%**
 - **Estimated construction start June 2023**
- **Piilani Highway Widening, Kilohana Drive to Wailea Ike Drive**
 - **Design at 60%**
 - **Estimated construction TBD**



Highways Division **Upcoming Projects**

- **Raised Crosswalks at Various Locations**
 - Estimated construction – December 2022
- **Haleakala Highway Reconstruction, N. Firebreak Road to Old Haleakala Highway**
 - Estimated start of construction – February 2023
- **Kekaulike Avenue ER Repairs at M.P. 8.2**
 - Estimated start of construction – February 2023
- **Kaaiea & Nailiilihaele Stream Bridge ER Repairs**
 - Estimated start of construction – March 2023
- **Honoapiilani Highway Shoulder and Guardrail Improvements**
 - Estimated start of construction – April 2023
- **Puunene Avenue Improvements Project**
 - Estimated start of construction – Summer 2023
- **Honoapiilani Highway Improvement Project**
 - Estimated start of construction – Spring 2025



Highways Division

State Highway Shoreline Protection Study

Thank you
